



# Monthly Progress Report

September 2023

Hempstead Union Free School District



Report prepared by Idris Mashriqi





# Table of Contents

**Section I – Program Summary**

**Section II – Work Progress** September 2023

**Section III – Work Projected for** October 2023

**Section IV – Progress Photos**

**Section V – Monthly Workforce Summary**



## Section I – Program Summary

### September 2023

#### **Project List**

- Hempstead UFSD - HS Infrastructure & Site Construction
- Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS
- Hempstead UFSD – Phase 1 Roof Replacements
- Hempstead UFSD – Phase 1 Window Replacements



## Section II - Work Progress September 2023

### **Hempstead UFSD - HS Infrastructure & Site Construction**

- **Laser Industries Inc.**
  - Completed Lacrosse netting Installation.
  - Training to district on removal and installation of lacrosse netting.
  - Completed painting lines for long jump section.
- **Nickerson Corp.**
  - Delivered and installed press box.
- **Musco/Relle**
  - Completed Electrical hookup to press box.

### **Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS**

- **Gatz Sitework & Landscape Construction.**
  - Completed the removal of electrical transformer.
  - Installed seeding, fertilizer and hydro seeding.



## Section II - Work Progress

### September 2023

#### Hempstead UFSD – Phase 1 Roof Replacements

- **More Contracting & Consulting. (High School)**
  - Completed roofing.
  - Completed metal copings.
  - Started skylight installation.
- **More Contracting & Consulting. (Paterson ES)**
  - Completed roofing.
  - Started painting and replacement of wood moldings.
  - Completed copper cap flashing.
  - Completed walk pads on roof.
- **More Contracting & Consulting. (ABGS MS)**
  - Completed roofing.
  - Prepped for metal panels.
  - Completed walk pads on roof.



## Section III - Work Planned October 2023

### **Hempstead UFSD - HS Infrastructure & Site Construction**

- Complete any open change orders.
- Complete all punch list work. (All trades)

### **Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS**

- No work planned.


### **Hempstead UFSD – Phase 1 Roof Replacements**

- **More Contracting & Consulting. (High School)**
  - Complete Sky Light Installation.
  - Complete open change orders.
- **More Contracting & Consulting. (Paterson ES)**
  - Complete metal coping.
  - Complete chimney cap.
- **More Contracting & Consulting. (ABGS MS)**
  - Complete metal panels.
  - Complete metal copings.





## Section IV – Progress Photos

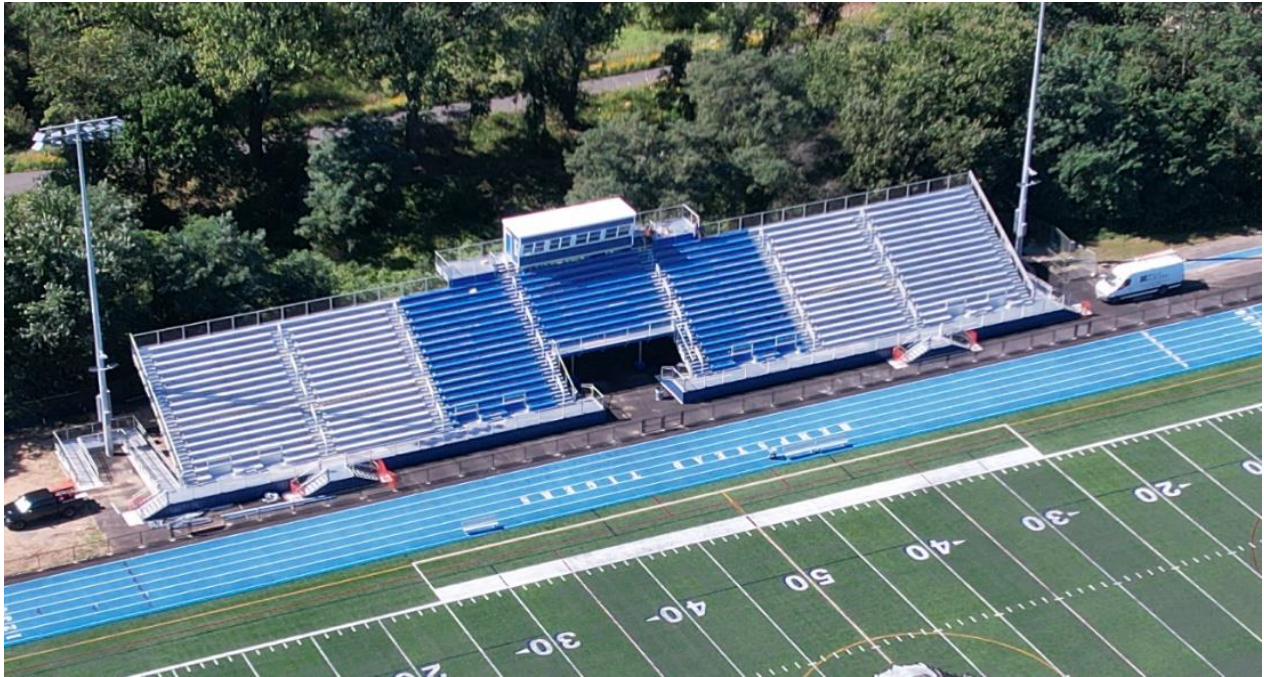


### Hempstead UFSD - HS Infrastructure & Site Construction





## Section IV – Progress Photos

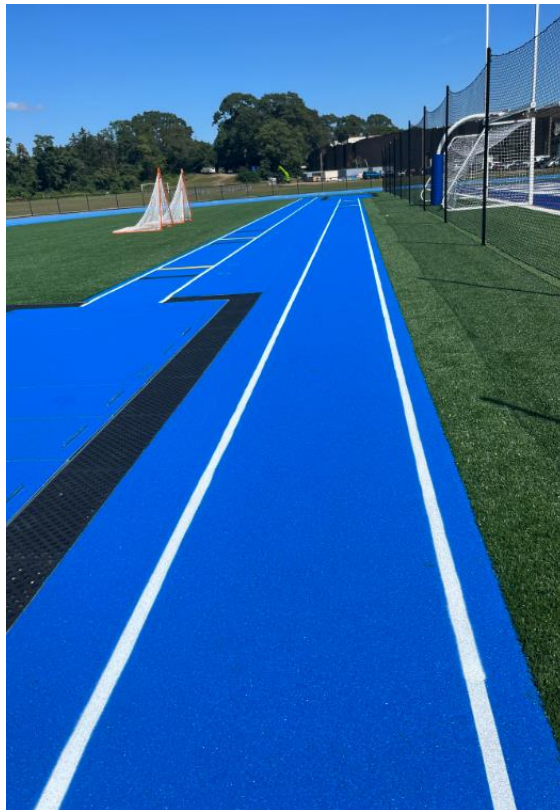

## Hempstead UFSD - HS Infrastructure & Site Construction





## Section IV – Progress Photos



Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS





## Section IV – Progress Photos



## Hempstead UFSD – Phase 1 Roof Replacements (High School)



## Section IV – Progress Photos




Hempstead UFSD – Phase 1 Roof Replacements (Paterson & ABGS)



## Section V – Workforce Summary – Company/Hours

### Hempstead UFSD - HS Infrastructure & Site Construction September 2023

#### ▼ MANPOWER GRAPH

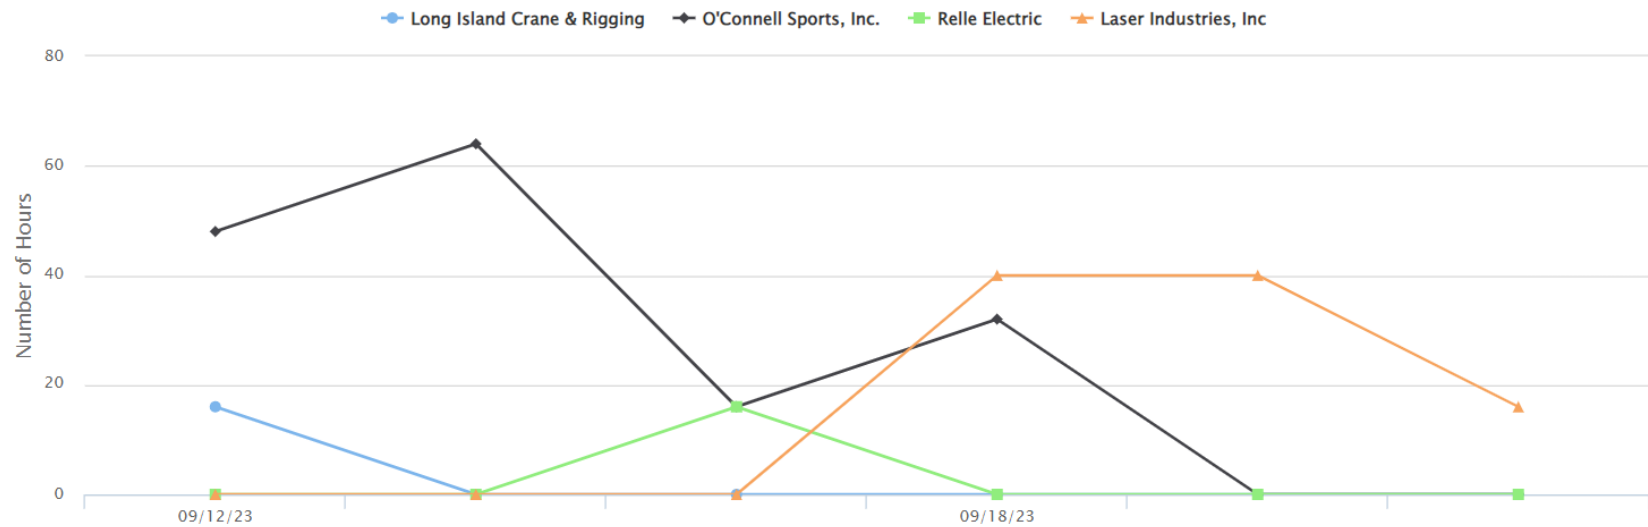




## Section V – Workforce Summary – Company/Hours

### Hempstead UFSD – Modular Disconnect & Removals @ ABGS MS September 2023

#### ▼ MANPOWER GRAPH

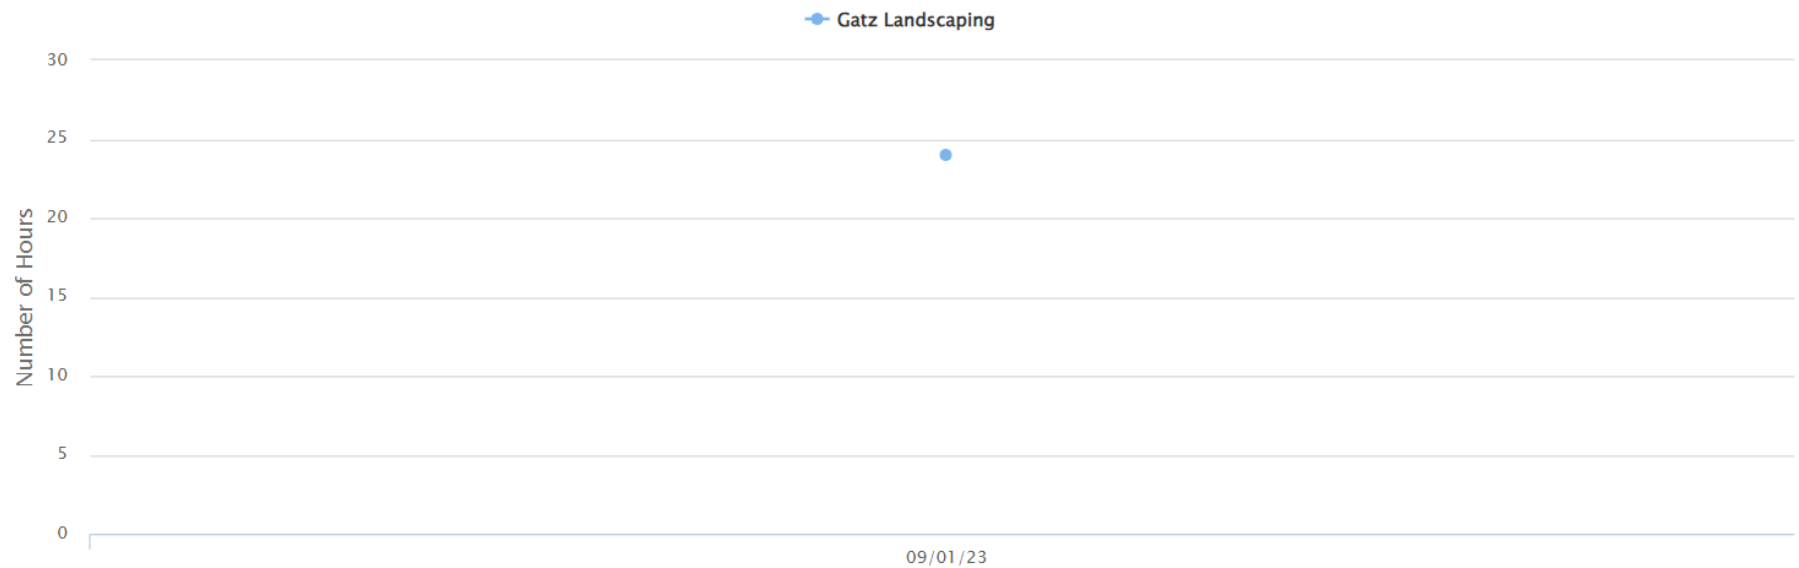






## Section V – Workforce Summary – Company/Hours

### Hempstead UFSD – Phase 1 Roof Replacements

### September 2023

#### ▼ MANPOWER GRAPH

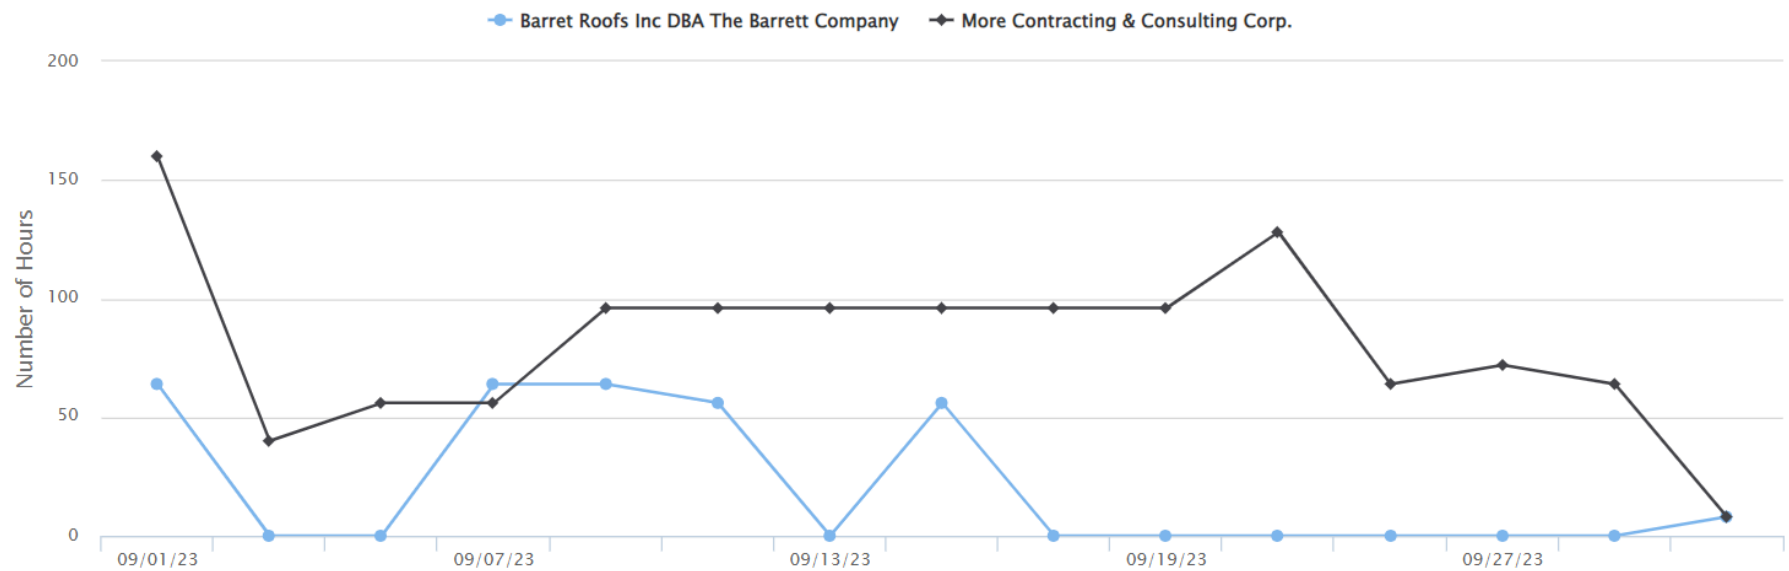



Hempstead Union Free School District  
September 2023

## **End of Progress Report**
